Sprint 1
2/12/2026
Scrum Master: Kyle Mazely
Team Members: Adam Taylor, Nolan Trent
Product Owner: Braeden Mullins

Goal

The primary objective of Sprint 1 was to establish the foundational gameplay mechanics for Appalachian Trail. This included implementing core player and enemy movement systems, configuring collision physics, setting basic idle and running animations, and beginning asset development by completing around 25% of the required game sprites. This sprint focused on laying the technical groundwork necessary for future gameplay features.

- Design and implement approximately 25% of planned sprites
- Create the main game scene and initialize the player character within the environment
- Implement responsive player movement through scripting on the player node
- Configure collision detection and physics interactions between player and enemy nodes
- Implement basic enemy behavior that allows enemies to move toward the player character
- Begin development of visual assets by completing 25% of the total sprites required for the game

User Stories Chosen for Sprint and Other Activities

- As a user, I want to be able to move my character so that I can navigate the game world and interact with the environment.
- As a user, I want animations so that gameplay feels smoother and more visually engaging.
- As a user, I want enemies so that there is challenge and interaction within the game.

Total Sprint Duration in Hours

- 3 members in team * 6 hours/week * 1 week/sprint = 18 man-hours available

List of Tasks Performed

Task	Owner	Status	Planned Hrs	Actual Hrs	Challenges
Designing Sprints	Adam	In Progress	5	6	Time constraints, lots of sprites to create, making sure artstyle is consistent among all sprites
Enemy Movement	Nolan	In Progress	7	7	Getting collision to work, making sure enemy is static, getting sprite to face player
Character Movement	Braeden	In Progress	6	5	Making sure there are no bugs with movement, making movement smooth, getting player to animate when moving or attacking

Review

- **Definition of Done (DoD):** The Definition of Done for this sprint required a fully movable player node, a functional enemy node capable of movement, and completion of 25% of the game's sprites.
- **Was the Goal Achieved? (Apply Details):** The sprint goal was partially achieved. The team successfully implemented player movement, enemy movement, and collision physics, meeting the technical gameplay requirements. However, the team did not complete 25% of the planned sprite assets. Unexpected snow days reduced overall productivity, particularly for asset creation and coordination-related tasks. This impacted sprite development more significantly than the coding tasks.
- **Feedback from Customers:** Feedback indicated that the implemented player and enemy mechanics were functional and visually promising. The product owner recommended prioritizing sprite completion in future sprints to improve visual consistency.
- **Focus for Next Sprint:** polishing up player movement and implementing a way to attack the enemies

Retrospective
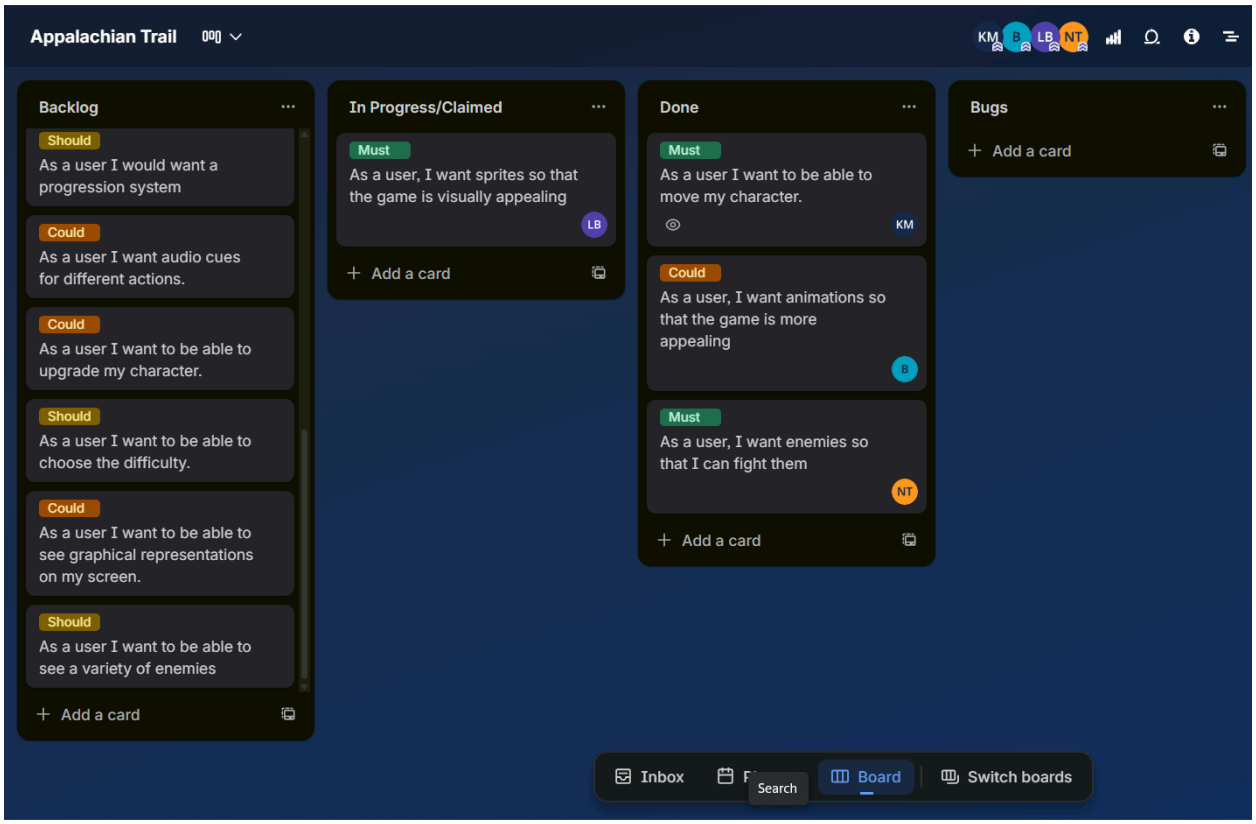
- **Changes to Scrum Process:** None.
- **Other Planned Adjustments?:** Sprite completion has been extended to Sprint 5 due to incomplete progress during this sprint.
- **Scrum Board:**
